



# East Worlington Parish Hall News|etter



## **Render and Window Project Edition 05 – 10 August 2018**

### **Rendering, Rendering and More Rendering**

This week has seen good progress with the rendering. Finishing coats have been applied to the east elevation, the south elevation and the southern end of the west elevation. The render is applied on one day and allow to dry slowly for 24 hours with final smoothing on the following day. When the render is applied, the walls are protected by canvas sheets. This is mainly to prevent the warm sun drying the render too quickly which can cause cracking through too rapid shrinkage. The protection is also against any rain that may fall and affect the drying process.



**East Elevation**



**South Elevation**



**West Elevation**



Supported by

**The National Lottery**<sup>®</sup>  
through the Heritage Lottery Fund



## Render and Window Project


### North Elevation

The North Elevation of the main barn is located above the kitchen. To gain access it has been necessary to erect scaffolding. Once in place work started to remove the old render and apply the new render in the three coat process – harl coat, scratch coat and finishing coat.



### Window and Render West Elevation

With the old window removed and the temporary board installed it was only possible to initially add a scratch coat to the west elevation. This is to ensure that when the repaired window was installed the final coat was applied there was a good seal between the wall and window..

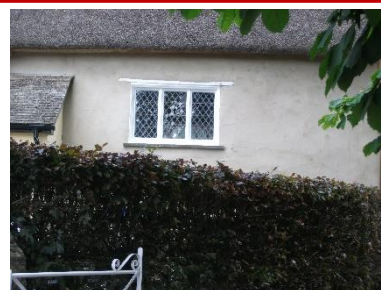

<http://www.eastworlingtonparishhall.btck.co.uk/>

<https://www.facebook.com/EastWorlingtonParishHall/>

<https://twitter.com/EWPHHeritage>

<http://ewparishhall.blogspot.co.uk/>

#### Key details:

For **bookings** please contact: **Lorna Manton**

Tel: 01884 860657

Email: [bookings@ewph.uk](mailto:bookings@ewph.uk)

Please contact us to discuss your particular requirements

